

PREPARED FOR MOTION MEDIA GROUP

# Two versions of Tubes. One live picture of the slate.

Martin, this is the full proposal behind the one-pager: how Tubes works, how a production company connects, and how MMG gets a live view across the productions it finances. Production companies run their productions in **Tubes Production**. Motion Media Group follows every production, every company and the group as a whole through **Tubes Portfolio**. Both sides work from the same live production data.

The proposition is simple: give the people running productions the tools they need to do the work, while giving MMG earlier, more reliable financial visibility, without adding another reporting layer or taking operational control away from the production companies.

The one-page summary and demo video accompany this proposal. The chapters that follow show how it works in practice, and how one real production can be used to prove it.

| PREPARED FOR                                            | FROM                       | SUBJECT                               | NEXT STEP                  |
|---------------------------------------------------------|----------------------------|---------------------------------------|----------------------------|
| Martin Waterman, VP<br>Acquisitions &<br>Co-Productions | Joachim de Blois,<br>Tubes | Portfolio-wide<br>financial oversight | Walkthrough & live<br>demo |

## CONTENTS

- |   |                                         |    |                                          |
|---|-----------------------------------------|----|------------------------------------------|
| 1 | Executive summary                       | 8  | AI for the work behind the work          |
| 2 | One system. Two views.                  | 9  | One plan, one source of truth            |
| 3 | Connect a company in minutes            | 10 | Built for a slate that crosses borders   |
| 4 | Keep Movie Magic. Make the budget live. | 11 | Who sees what, by design                 |
| 5 | From budget to final cost, always live  | 12 | Gradual by design, starting with a pilot |
| 6 | Invoices & accounting                   | 13 | Capability checklist                     |
| 7 | One live view across the slate          |    |                                          |

## CHAPTER 1 · EXECUTIVE SUMMARY

# One production. Four things to prove.

This proposal is built around one decision: can Tubes give MMG earlier, more reliable financial visibility across its productions, without taking operational control away from the companies running them? The pilot tests four things.

### 1 · EARLIER

#### **See movement before the report**

Do commitments and the estimate to complete move the EFC early enough to show a developing problem before the normal reporting cycle?

### 2 · COMPARABLE

#### **One structure across companies**

Can different production companies work in their own way while reporting through a consistent financial structure at group level?

### 3 · LESS MANUAL

#### **Consolidation without assembly**

Does MMG get a live portfolio view without teams spending time collecting, reconciling and consolidating separate reports?

### 4 · NON-INTRUSIVE

#### **Visibility without takeover**

Can a production company continue to run its production, workflows and financial operations while MMG gets the visibility it needs?

One real production is enough to answer these questions. The chapters that follow show how Tubes works, how the connection is made, and how the pilot can prove it in practice.

## One system. Two views.

Tubes has two sides to it. Production companies use Tubes to run their productions; MMG uses Tubes Portfolio to see and steer what is happening across the group. Both work from the same live production data.

That distinction matters. MMG does not need to operate inside a production company's books to know where things stand. Portfolio is a management and control layer on top of the live data, not another dashboard built from reports that someone has to assemble.

FOR MOTION MEDIA GROUP

### MMG Tubes Portfolio

- One live view across every connected company and production
- Early warnings when a forecast moves beyond budget
- Cashflow and margin forecasts by company, month, quarter and year
- Price per minute and per episode, comparable across the slate
- Drill-down from portfolio → company → production → invoice
- Read-only share links for investors and clients
- Standard setup and templates, rolled out group-wide

**Follow and steer the slate without running the productions.**

FOR EVERY COMPANY OR PRODUCTION MMG FINANCES

### Tubes Production

- One or more productions and series in each workspace
- Build budgets in Tubes or import existing Movie Magic budgets
- Real-time cost control from budget to PO to invoice to forecast
- Invoice processing, automatic reading and approvals
- Xero and other accounting connections when wanted
- Day planning, call sheets and crew app, all on the same data
- Local currency and language by company, with fixed exchange rates per production

**Run the production. Head office sees the rollup.**

THE PORTFOLIO ROLE

For an investor, holding company or group management team: roll out a standard Tubes setup across the companies you finance, then follow every production, every company and the group as a whole, without taking over the day-to-day running of the productions.

# Connect a company in minutes

Joining Tubes starts with a simple signup link. The company gets its own workspace, pre-configured with the group's structure and standards, and can start working straight away. How quickly it adopts the wider workflow is up to the team; the phased path comes in Chapter 12.

## 1 MMG sends the signup link

The link carries the group setup: cost structure, roles, approval rules and, where useful, standard budget and format templates.

## 2 The company creates its workspace

Self-onboarding takes around five to ten minutes. The workspace arrives pre-configured, so companies across the group can work in their own environment while using the same underlying structure and reporting standards.

## 3 The connection is live

As soon as the company starts creating projects and recording data, its numbers can roll up into the MMG portfolio automatically and in real time. No separate reporting process is required.

## 4 Support where it matters

We support teams through signup, provide training where it is useful, and stay close until they are comfortable running independently. Most teams should need very little support, but it is there whenever they do.

Tubes · Account setup, the signup wizard

PROGRESS

Step 1 of 6

1

Company profile

Name, email & address

±1 min

2

Logo & avatar

Make it recognisable

±1 min

3

Team

Collaborate

±1 min

4

Appearance

Your own style

30 sec

5

Settings

Numbers & currency

30 sec

6

Administration

Budget process & roles

±1 min

7

Xero

Connect accounting

Optional

Your data is safe. Everything can be changed later.

Ready in a few minutes

### Tell us about your company

Fill in the basics and you're good to go. You can always update this later.

Individual

Company

Organization

Team

Account name

Company name

Northside Pictures

e.g. Johnson Productions

Email address

Country

production@northside.ca

Canada

Next: Logo & avatar →

The signup wizard itself. Six short steps; the time estimates next to each step are the product's own, and they add up to about five minutes. That is the workspace setup for a new company: this wizard, pre-filled by your group profile. Operational adoption follows at the team's own pace.

Motion Media Group

Tubes Portfolio · portfolio rollup, drill-down into every production

Off

Vendor

Portfolio

TUBES PRODUCTION

Company A

3 productions connected

TUBES PRODUCTION

Company B

1 production connected

TUBES PRODUCTION

Company C

2 productions connected

NEXT SIGNING

Joins via your signup link

Workspace setup in minutes

CHAPTER 4 · BUDGETS & MOVIE MAGIC

# Keep Movie Magic. Make the budget live.

Teams can build budgets directly in Tubes, with cost groups, versioning, scenario comparison, a locked approved baseline and a separate work budget for day-to-day control. But most teams won't need to rebuild anything: they can simply import their existing Movie Magic budget, which becomes the live baseline in minutes.

Keep Movie Magic if it works for the team, or build the budget directly in Tubes. Either way, Tubes picks up where budgeting leaves off, turning the budget into a live production model connected to commitments, actual costs, forecasts and the rest of the production.

Keep the tools that work. Connect the information that matters.

Tubes · Projects in production

Projects in Production

Demo Tubes

Create a budget

Start from a template, copy an existing one, let AI draft it, or import Movie Magic.

Generate AI Budget

Create New Budget

All (8)

Development (3)

Production (4)

Post Production (1)

FF

Fox and the Forest

Development

Project start

22 feb 2026

Delivery

20 jun 2026

SW

The Secret of the Wadden, Part 1

Production

Project start

10 sep 2024

Delivery

13 feb 2025

ET

Echoes of Tomorrow

Post Production

Project start

3 jan 2025

Delivery

19 sep 2025

The projects home of a production company: every production with its status and dates. A budget starts from a template, a copy of an earlier production, an AI draft, or a Movie Magic import. Demo data, illustrative.

Tubes · Budget builder

Budget

Additional costs

€ 64.625

Budget incl. additional

€ 76.600

Sales incl. additional

Lock version

Budget published, editing not possible

Sort: Cost group

Hide Sales

| ITEM                                   | QTY | UNIT     | UNIT PRICE | BUDGET   | SALES    |
|----------------------------------------|-----|----------|------------|----------|----------|
| DEVELOPMENT                            |     |          |            | € 35.700 | € 44.800 |
| Head writer<br>Treatment + pilot       | 20  | Days     | € 850      | € 17.000 | € 22.000 |
| Script coach<br>2 sessions per episode | 12  | Sessions | € 600      | € 7.200  | € 9.000  |
| Format bible<br>Design + rights        | 1   | Fixed    | € 11.500   | € 11.500 | € 13.800 |
| RECORDING ON LOCATION                  |     |          |            | € 18.550 | € 26.050 |
| Camera set 01<br>2x FX9 + lenses       | 7   | Days     | € 1.850    | € 12.950 | € 18.200 |
| Sound + DIT<br>Location sound          | 7   | Days     | € 800      | € 5.600  | € 7.850  |
| STORY & RIGHTS                         |     |          |            | € 1.000  | € 1.250  |
| MONTAGE                                |     |          |            | € 3.500  | € 4.500  |
| Totals                                 |     |          |            | € 58.750 | € 76.600 |

The budget builder: cost groups with budget and sales side by side, and a locked, published version as the approved baseline. Whether a budget is built here or arrives through Movie Magic import, this is the live baseline that commitments, invoices and the forecast attach to. Demo data, illustrative.

HOW THEY COMPARE


| ASPECT            | MOVIE MAGIC                              | TUBES                                                      |
|-------------------|------------------------------------------|------------------------------------------------------------|
| What it is        | A budgeting document                     | A live production model                                    |
| Working           | One file, usually with the line producer | Multi-user cloud workspace, the whole team in one place    |
| Scope             | Ends when the budget is done             | Connects the budget to POs, invoices, actuals and forecast |
| During production | Updated by hand, shared as versions      | EFC and variance move the moment something is committed    |
| Group view        | Someone has to send a file               | MMG follows every production live in Tubes Portfolio       |
| Beyond the money  | —                                        | Planning, call sheets and the crew app on the same data    |

# From budget to final cost, always live

Tubes keeps the full cost picture moving in real time. Every purchase order and invoice is linked to a budget line. That simple discipline connects the original budget to what the production is working with, what it has committed, what it has spent and what it now expects to spend.

The moment a PO is raised, committed cost and the forecast final cost update. As invoices and other transactions arrive, actual cost follows. Each team can see its own position and variance as the production moves, without waiting for a month-end cost report to discover where it stands.

## THE SIX NUMBERS

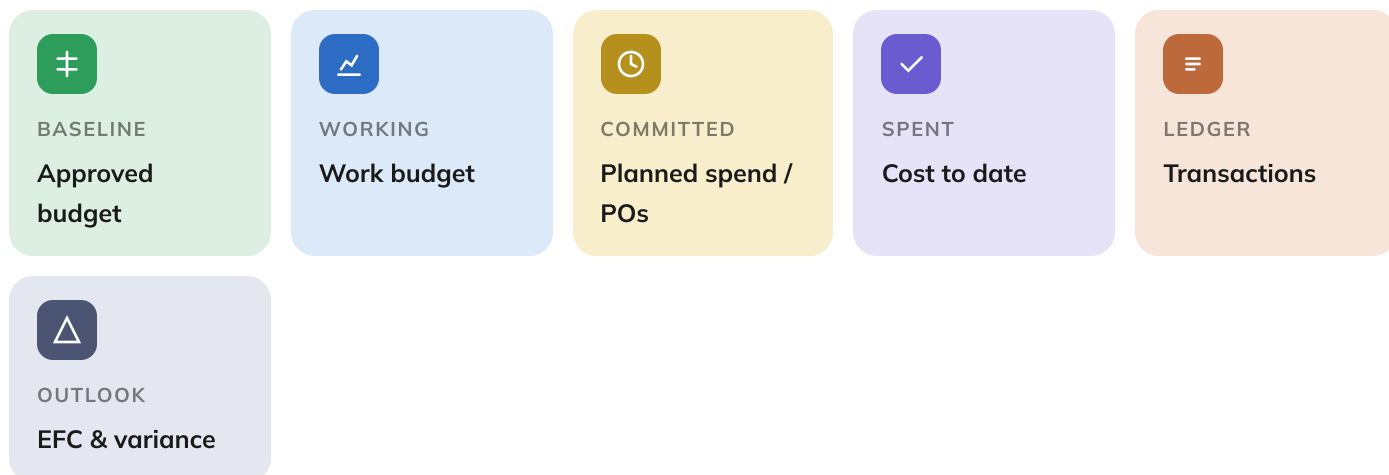

The model stays consistent from first budget to final cost: **approved budget → work budget → committed → actuals + estimate to complete → EFC**. Variance and cash requirements follow from the same underlying data. Transactions are not a separate reporting stage; they are the inputs that build cost to date. The forecast therefore stays anchored to what has actually been spent and committed, while the team's remaining expectations are captured in the estimate to complete.




## CHAPTER 6 · INVOICES & ACCOUNTING

# From inbox to books, without re-keying

How it works: an invoice is dropped in (or mailed in), and Tubes reads it, supplier, amounts, dates, and proposes the budget line it belongs to. A person confirms; approval rules route it to whoever has to sign off at that amount. Once approved, it counts in cost to date and the forecast, immediately.

If the company uses **Xero or other accounting software**, the connection keeps the production ledger and the books aligned, no double entry, no month-end surprise where the two disagree. Teams that prefer exports get exports.

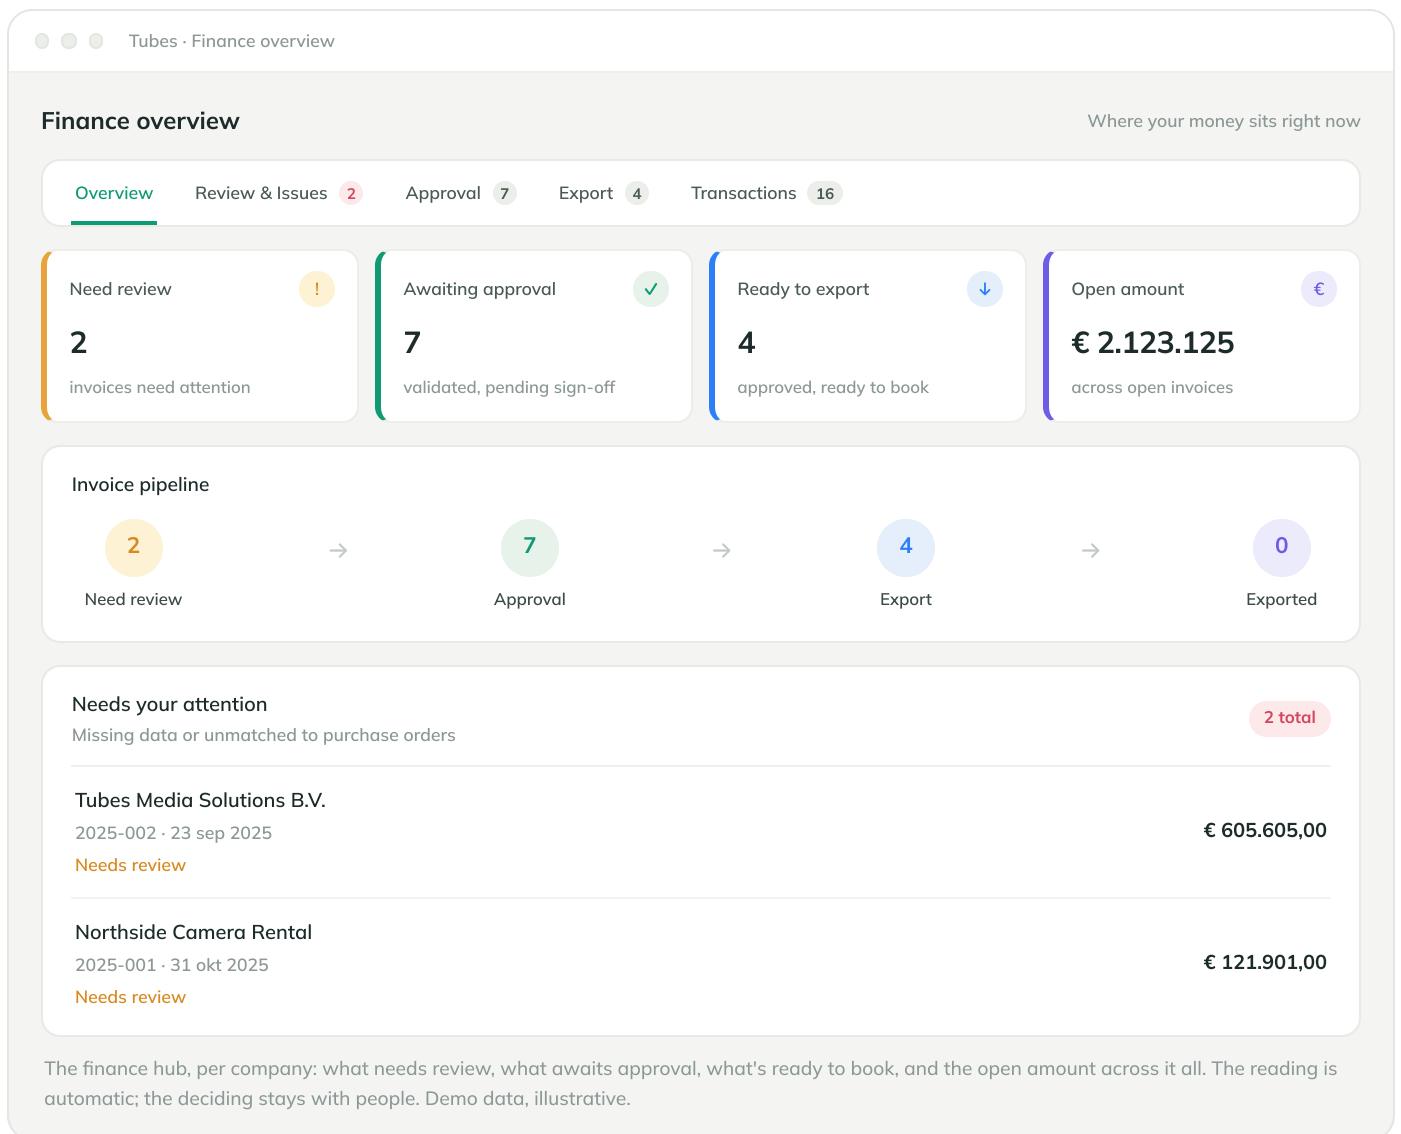

## CHAPTER 7 · THE PORTFOLIO DASHBOARD

# One live view across the slate

From the portfolio workspace, MMG can see every production across every connected company in one place, in real time. Progress, commitments, costs and forecasts are pulled directly from the live production data, not assembled into a separate report.

That means the portfolio view stays current as the productions move. MMG can move from the group picture into the detail behind it, while each production team continues working in its own workspace. One set of data serves both the people running the production and the people overseeing the slate.

| PRODUCTION                                   | STATUS            | BUDGET       | COMMITTED    | COST TO DATE | EFC          | VARIANCE   |
|----------------------------------------------|-------------------|--------------|--------------|--------------|--------------|------------|
| Northern Crossing<br>Company A · Feature     | ● Production      | \$8,400,000  | \$6,120,000  | \$4,385,200  | \$8,361,000  | +\$39,000  |
| The Long Season<br>Company A · Series, 8 eps | ● Production      | \$12,000,000 | \$9,870,000  | \$7,214,900  | \$11,986,000 | +\$14,000  |
| Salt Water<br>Company B · Feature            | ● Post production | \$5,150,000  | \$5,020,000  | \$4,890,400  | \$5,102,000  | +\$48,000  |
| Fireline<br>Company C · Documentary          | ● Approved        | \$1,900,000  | \$310,000    | \$122,600    | \$1,900,000  | —          |
| Portfolio                                    |                   | \$27,450,000 | \$21,320,000 | \$16,613,100 | \$27,349,000 | +\$101,000 |

Illustrative figures. In the live product every number drills down, portfolio → company → production → budget line → the individual invoice or PO behind it.

Tubes · Cost type detail, the bottom of the drill

Project: Fox and the Forest · Forecast · Cost type: 1002, BUDGET DEVELOPMENT

BUDGET

WORK BUDGET

PLANNED

COST TO DATE

EFC

VARIANCE

€ 10.000

€ 10.240

€ 3.000

€ 2.400

€ 5.400

€ 4.600

Cost to date

Planned

Remaining budget

1 planned cost not yet linked to a transaction

Link now

Planned costs & PO's

2 items · 1 to link

To link

Scenario workshop, writers room

Storyline BV · 3 days, incl. location

€ 2.000

Linked

Research trip Ardennes

Recce + location photos · € 900 linked

€ 1.000

Expectations total

€ 3.000

Cost to date

Transactions linked to planned costs

Invoice, writers room day 1–2

Storyline BV · Invoice 2026-114 · linked to: Scenario workshop

€ 1.500

Freelance script editor

M. van Dijk · Invoice 2026-131 · linked to: Research trip Ardennes

€ 900

Cost to date total

€ 2.400

The bottom of the drill: one cost type of one production. Every PO and every invoice is linked to the budget line it belongs to, which is exactly why the portfolio numbers above can be trusted. Anything unlinked is flagged until someone deals with it. Demo data, illustrative.



### Early warnings

The dashboard flags a production the moment its forecast moves past budget, at commitment time, weeks before it would surface in a cost report.



### AI analysis

AI analyses support the group view: the assistant reads along with the numbers and flags what deserves attention, at group level and on set.

The same slate also reads as a **cashflow and margin forecast overview per production company**, switchable between month, quarter and year. For a capital-recycling model, this is the view that matters: when does cash go out, when does it come back, and what margin is each company on course to deliver.

Month

Quarter

Year


| COMPANY                                         | SEP 2026     | Q4 2026      | FY 2026      | MARGIN · FY 2026 |
|-------------------------------------------------|--------------|--------------|--------------|------------------|
| <b>Company A</b><br>2 productions in production | -\$1,240,000 | -\$2,850,000 | -\$5,400,000 | 14.2%            |
| <b>Company B</b><br>Delivering                  | +\$380,000   | +\$1,050,000 | +\$1,620,000 | 11.8%            |
| <b>Company C</b><br>Pre-production              | -\$210,000   | -\$640,000   | -\$980,000   | 17.5%            |
| <b>Portfolio</b>                                | -\$1,070,000 | -\$2,440,000 | -\$4,760,000 | 14.6%            |

Illustrative figures. Company A is in peak production (cash going out); Company B is delivering (cash coming back). The margin column is the forecast at completion, per company, from the same live production data.

Per production, the same forecast also reads as a **forward-looking cash requirement**: funding tranches in, spend drawing the position down, and a flag when the next tranche is needed.

## Forward-looking cash requirement

One feature film: tranches in, spend out, next tranche flagged ahead of time. Illustrative

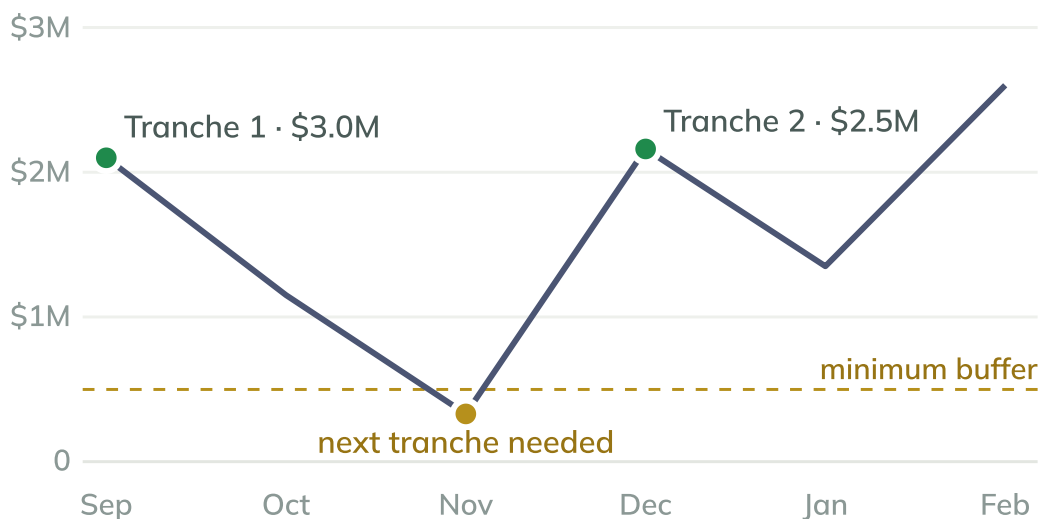

Built from the production forecast, expected payment timing and funding tranches; receivables and incentives can be added where available. The same view rolls up per company and for the portfolio.

The same forecasts add up to the picture an investor actually asks about: how much capital is at work across the slate, and when it comes back.

## Capital at work across the slate

Deployed capital per month, deliveries bringing it back. Illustrative



Built from the production forecast, expected payment timing and funding tranches; receivables and incentives can be added where available. Deliveries bring capital plus margin back, and the live forecast shows when it comes free and when new commitments will need it. Illustrative.

And because every production carries its running time and episode count, the dashboard also shows the **unit economics**, the numbers your acquisitions side thinks in:

SERIES

**\$1.56M / episode**

The Long Season, forecast cost per episode, against a \$1.50M budget target.

FEATURE

**\$79k / finished minute**

Northern Crossing, 106 finished minutes on an \$8.4M budget.

COMPARABLE

**Same metric, every production**

Price per minute and per episode, computed from live forecasts, comparable across the whole slate.

Budgets and status snapshots can also be shared with outside stakeholders through **read-only links**, so investor reporting draws on live numbers instead of assembled spreadsheets.

---

CHAPTER 8 · AI IN TUBES

## The assistant behind the production

AI in Tubes is there to remove the reading, checking and drafting that consumes production-finance time, not to make decisions on people's behalf. Every AI-generated suggestion is clearly identified, and every decision remains with a person. In Tubes, violet marks the assistant, so you always know what came from AI.



### Draft budgets

Describe the production, format and target amount, and the assistant creates a first budget for the team to refine. It gets a production to a workable starting point faster, particularly for recurring formats. The assistant drafts; the team decides.



### Read invoices and documents

Invoices are read automatically and key information is extracted: supplier, amounts, dates and a proposed budget line. A person confirms the result, and approvals remain human.



### Watch the numbers

As a production runs, the assistant monitors costs against budget and flags what deserves attention: by team or department on the production, and rolled up across the group for MMG.



### Learn from the finish

When a production wraps, the assistant compares budget to final cost by cost type and highlights what the next production could do differently.



### Translate automatically

Language does not have to be a barrier. The assistant translates between Tubes' ten supported languages, so an international production team and head office can work from the same information in their own language.

Every suggestion is visible, attributable and reversible. AI usage is managed through monthly credits per workspace, keeping the cost predictable.

## Where it's heading

The ambition is simple: empower productions to spend more time making things and less time reconciling spreadsheets, while giving the people financing them a live view of where things stand.

AI takes that further. The direction is towards operating Tubes through conversation: ask a question and get a live answer; give an instruction and have

the assistant prepare the work for a person to review and approve. The system does the work around the decision. The person stays in control.

#### Tubes Assistant

How is The Long Season doing against budget?

It's **\$14k under**, the tightest margin on the slate. EFC is **\$11.99M** against a **\$12.0M** budget, with cost type 2000 CREW closest to its line. Want the breakdown per line?

Yes, and prepare a note for Thursday's production meeting.

Breakdown is open on your screen. The note is drafted and waiting for your approval before it goes to the team.

---

## CHAPTER 9 · PLANNING, CALL SHEETS & CREW

# One plan, one source of truth

Production teams plan their days in Tubes, build call sheets directly from that planning, and publish them when they're ready. Schedules and published call sheets then land straight on the crew's phones through the Tubes mobile app: no PDF chains, no version confusion, no wondering which document is current.

And because the production plan sits alongside the budget, the operational and financial pictures stay connected. The people planning the work and the people tracking the money are working from the same underlying data, rather than maintaining two separate versions of the production.

Tubes · Planning

Planning10 aug 2026 – 16 aug 2026

CalendarCallsheets

| MONDAY<br>10                                                                                                                                 | TUESDAY<br>11                                                            | WEDNESDAY<br>12                                                                                                                   | THURSDAY<br>13                                                                                                                                     |
|----------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------------------------------------------|
| <div>07:00 – 19:00<br/>Shoot day 12 · The Long Season<br/>Studio 4</div> <div>20:00<br/>Dailies review<br/>Online · director &amp; DoP</div> | <div>07:00 – 19:00<br/>Shoot day 13 · The Long Season<br/>Studio 4</div> | <div>09:00 – 13:00<br/>Location scout<br/>Unit manager</div> <div>14:00 – 17:00<br/>Tech recce<br/>The Secret of the Wadden</div> | <div>08:00 – 18:00<br/>Shoot day 14 · The Long Season<br/>Location: Westergas</div> <div>10:00<br/>Cast fitting<br/>Reality &amp; Competitie</div> |

Callsheets

Per shooting day, status, distribution and crew

+ New callsheet

|           |                                                       |               |         |
|-----------|-------------------------------------------------------|---------------|---------|
| 10<br>AUG | <b>Callsheet #12</b><br>The Long Season · S1          | 07:00 / 19:00 | Sent    |
| 13<br>AUG | <b>Callsheet #14</b><br>The Long Season · S1          | 08:00 / 18:00 | Draft   |
| 17<br>AUG | <b>Callsheet #01</b><br>The Secret of the Wadden · S1 | 06:30 / 17:30 | Planned |

One week of a production: shoot days, prep and post side by side, and the callsheets that go with them. "Sent" means the crew already has it on their phones. Demo data, illustrative.

## CHAPTER 10 · CURRENCIES & LANGUAGES

# Built for a slate that crosses borders

Your productions already span jurisdictions, from Canada and Puerto Rico to India and Africa. Tubes is built for that reality from the start, with local currencies, local workflows and multilingual access, while giving the group a consistent view across the slate.

#### CURRENCY

##### **Local currency, fixed FX**

Each production company works in the currency it actually uses. Budgets, purchase orders and invoices stay in local currency, with a fixed exchange rate set for each production. The group can then report in a common currency without teams having to convert anything manually or worry about exchange-rate movements distorting the production budget.

#### LANGUAGE

##### **10 languages**

Tubes supports 10 languages, set at workspace or individual-user level. A Dutch line producer and a Canadian accountant can work on the same production, each in their own language. Additional languages can be added as needed.

#### GETTING STARTED

##### **Live in minutes, not weeks**

A workspace can be set up quickly using standard templates and configuration. There is no need for a lengthy implementation project before a team can start working.

**How it works across borders.** The production company works entirely in its own local currency. Tubes handles the fixed exchange rate at production level, allowing the group rollup to report consistently without changing the underlying numbers.

#### COMPANY A · CANADA

##### **Works in CA\$**

Budgets, POs and invoices in Canadian dollars

#### COMPANY B · NETHERLANDS

##### **Works in €**

Entirely in euros, including the Xero connection

#### COMPANY C · PUERTO RICO

##### **Works in US\$**

Entirely in US dollars

### **One portfolio, one reporting currency**

Exchange rates fixed per production and applied consistently across the rollup, and every converted number still drills down to its local-currency source

---


## CHAPTER 11 · DATA SEPARATION & PERMISSIONS

# Who sees what, by design

Every production company works in its own, separate workspace. Its data belongs to that company, with its own permissions and controls. MMG's portfolio workspace provides the group-level view, with the ability to drill into the productions it finances, without operating inside the company's books. Companies remain fully separated from one another.

Within each workspace, **role-based permissions** determine exactly who can see and do what. A line producer sees the productions they work on. A department head can be limited to their own work budget. An accountant can have access to the financial information they need without necessarily seeing rates. Approval rules can put a named person between a significant commitment and the money.

This same separation works at group level. MMG gets the transparency it needs across the productions it finances, while each company keeps control of its own data and operations. Portfolio access is read-only: MMG can see and drill into the data, but cannot edit it.

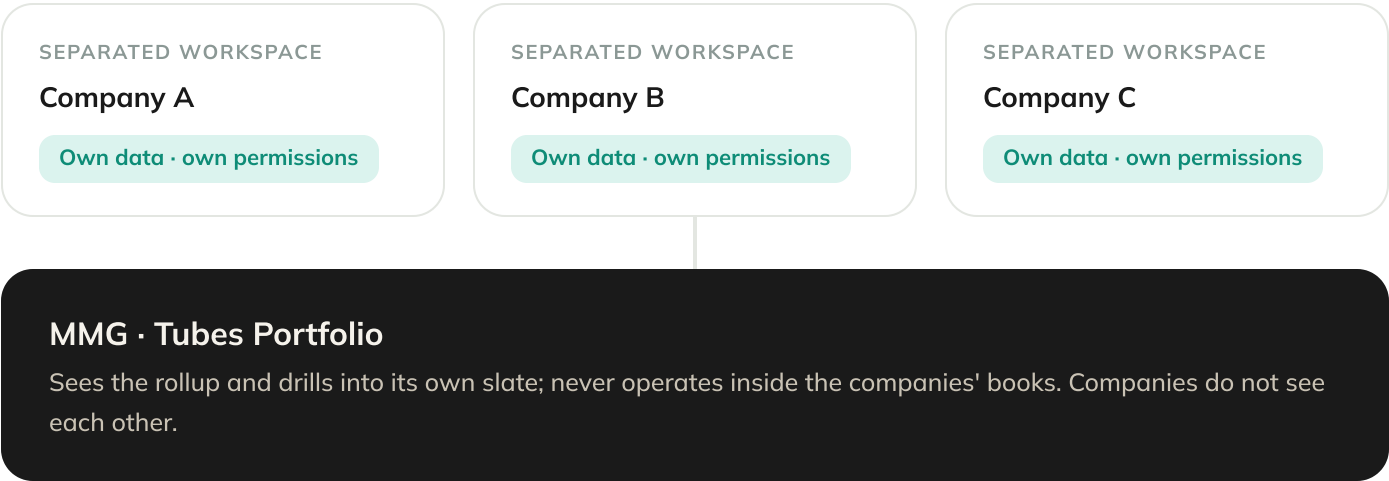

| ROLE                                                | PRODUCTION DETAIL      | RATES & SALARIES | FINANCE | GROUP ROLLUP |
|-----------------------------------------------------|------------------------|------------------|---------|--------------|
| <b>Line producer</b><br>runs the production         | ● Full                 | ● Full           | ● Full  | —            |
| <b>Department head</b><br>own work budget           | ● Own lines only       | —                | —       | —            |
| <b>Accountant</b><br>books & export                 | ● Full                 | —                | ● Full  | —            |
| <b>MMG · Tubes Portfolio</b><br>read-only oversight | ● Read-only drill-down | —                | —       | ● Full       |

How to read this: "Full" means the role sees and works in that area; "Own lines only" limits a department head to their own budget lines; the dash means no access. Illustrative permission set: every workspace defines its own roles and approval rules, this is a typical shape, not a fixed one.

# Gradual by design, starting with a pilot

Tubes doesn't ask a team to change the way it works all at once. Start with the data you already have, get visibility from day one, then bring more of the workflow into the system when the team is ready. Each team can move at its own pace, while the value builds from the start.

1

## Import and see

Workspaces created via your signup link. Current Movie Magic budgets imported. Costs start landing against budget lines. Your portfolio view is live.

First

2

## Control

Approval rules, forecasts and expectations, the accounting connection. Overruns surface at commitment time, group-wide.

Then

3

## Run

Day planning, call sheets and the crew app, production operations on the same data as the money.

When a team wants it

## The pilot

The quickest way to judge this is to look at one of your own productions through it.

- ✓ **Pick one production you finance.** Its team signs up through your link and imports its current budget.
- ✓ **Set up the MMG portfolio workspace,** configured with your standard setup and templates, ready to roll out further later.
- ✓ **Follow the production live:** budget, commitments, cost to date and forecast, from the portfolio dashboard down to the invoice.
- ✓ **Then decide.** If the picture isn't sharper than what you have today, that is the end of it.

Plan the walkthrough

or write me directly, [joachim@tubes.media](mailto:joachim@tubes.media)

# What's in the box

A complete overview of Tubes. Every role in the team gets the functionality, workflows and tools they need to do their job effectively, all in one system that brings the whole production together.

And Tubes keeps growing. We're continually covering more of the production process and taking administrative work off people's hands, leaving more time and headspace for the creative work.

## Develop & budget

- ✓ Project setup, briefing and funding
- ✓ Format templates, reusable across productions
- ✓ Budget builder with versions and a locked baseline
- ✓ Movie Magic budget import
- ✓ Budget compare for scenarios
- ✓ Commercial proposals for clients and commissioners
- ✓ AI budget drafting support (early version)
- ✓ Project documents, images and links in one place

## Plan & produce

- ✓ Day planning and scheduler
- ✓ Scenes & breakdown, stripbook (in development)
- ✓ Casting, recruitment and cast & crew management
- ✓ Locations
- ✓ Call sheets with status and distribution
- ✓ Crew app: schedules and callsheets on every phone
- ✓ Editing and delivery tracking
- ✓ Production dashboard per shoot day

## Control the money

- ✓ Work budgets per team member or department
- ✓ Planned costs and purchase orders
- ✓ Operational invoice processing with automatic reading
- ✓ Approval rules and transaction approval
- ✓ Transactions linked to budget lines

## Oversee & share

- ✓ MMG Tubes Portfolio: rollup over every company and production
- ✓ Cashflow and margin forecasts by month, quarter and year
- ✓ Early warnings when a forecast moves past budget
- ✓ AI analyses (early version)

- ✓ Live forecast and EFC, with views per role
- ✓ Cost reports: budget versus actuals per period, with historical snapshots
- ✓ Local currency per company, fixed exchange rates per production
- ✓ Xero and other API accounting connections

- ✓ Price per minute and per episode across the slate
- ✓ Read-only share links for investors and clients
- ✓ Role-based permissions and separated workspaces
- ✓ Signup links, standard setup and group-wide templates
