

PREPARED FOR MOTION MEDIA GROUP

Two versions of Tubes. One live picture of the slate.

Martin, this is the full proposal behind the one-pager: chapter by chapter, how Tubes does what it claims. Production companies run their productions in **Tubes Production**; Motion Media Group follows every production, every company and all companies together in **Tubes Portfolio**. A one-page summary and a demo video accompany this document.

PREPARED FOR	FROM	SUBJECT	NEXT STEP
Martin Waterman, VP Acquisitions & Co-Productions	Joachim de Blois, Tubes	Portfolio-wide financial oversight	Walkthrough & live demo

CONTENTS	
1 Executive summary	8 AI in Tubes
2 Two versions of Tubes	9 Planning, call sheets & crew
3 Getting connected	10 Currencies & languages
4 Budgets & Movie Magic	11 Data separation & permissions
5 Cost control in real time	12 Adoption path & pilot
6 Invoices & accounting	13 Capability checklist
7 The portfolio dashboard	

What the pilot needs to prove

Everything in this proposal serves one decision: connect one real production and test whether Tubes gives MMG earlier, more reliable financial visibility without taking operational control away from the production company. Four questions decide it.

EARLIER

Forecast movement before the reporting cycle

Do you see commitments and ETC move the EFC before the normal report would show it?

COMPARABLE

One financial structure across companies

Can different production companies report through the same structure?

LESS MANUAL

Consolidation without assembly

Does MMG spend less time collecting and consolidating reports?

NON-INTRUSIVE

Visibility without takeover

Does the production company keep running its production, workflows intact?

The chapters that follow explain how Tubes intends to prove those four things with one real production.

CHAPTER 2 · TWO VERSIONS OF TUBES

One follows. The other runs.

Tubes is production software with management overviews on top, for one or more underlying production companies. The companies work in it; Motion Media Group watches over it. That distinction matters, because it means MMG never has to operate inside a production's books to see what is happening in them. Tubes Portfolio is a control layer built on the live production data underneath, not another dashboard fed by reports.

FOR MOTION MEDIA GROUP

MMG Tubes Portfolio

- One live view over every connected production, built on the data underneath
- Early warnings the day a forecast moves past budget
- Cashflow and margin forecast per company, month, quarter, year
- Price per minute and per episode, comparable across the slate
- Drill-down: portfolio → company → production → invoice
- Read-only share links for investor reporting
- Standard setup and templates, rolled out group-wide

Follow and steer, without running the productions.

FOR EVERY COMPANY OR FILM YOU FINANCE

Tubes Production

- One or more productions and series per workspace
- Create projects; build budgets or import Movie Magic directly
- Real-time cost control: budget → PO → invoice → forecast
- Invoice processing with automatic reading and approvals
- Xero or other accounting software, connected when wanted
- Day planning, call sheets and a crew app on the same data
- Local currency and language per company; fixed exchange rates per production

Run the production, head office sees the rollup.



FROM THE PRODUCT, THE PORTFOLIO ROLE

"An investor, holding or group management. Rolls out a standard Tubes setup to its companies and follows every production, every company and all companies together."

CHAPTER 3 · GETTING CONNECTED

How a production company joins

The connection is a weblink. Workspace setup takes minutes; operational adoption is gradual, along the phased path in chapter 12.

1

MMG sends its signup link

The link carries your group profile: cost structure, roles, approval rules and, optionally, your standard budget and format templates.

2 The company creates its own workspace

Five to ten minutes of self-onboarding. The workspace arrives pre-configured, so every company across the group starts from the same structure and reports the same way.

3 The connection is live

From the first project the team creates, its numbers roll up into MMG's portfolio dashboard, automatically, in real time.

4 Support when needed, where needed

We support companies during signup, give training where that helps, and stay involved until a team runs on its own. Most teams need little of it; the point is that the help is there.

Tubes · Account setup, the signup wizard

PROGRESS

Step 1 of 6

- 1 Company profile** ±1 min
Name, email & address
- 2 Logo & avatar ±1 min
Make it recognisable
- 3 Team ±1 min
Collaborate
- 4 Appearance 30 sec
Your own style
- 5 Settings 30 sec
Numbers & currency
- 6 Administration ±1 min
Budget process & roles
- 7 Xero Optional
Connect accounting

Your data is safe. Everything can be changed later.

● Ready in a few minutes

Tell us about your company

Fill in the basics and you're good to go. You can always update this later.

Individual

Company

Organization

Team

Account name

Company name

Northside Pictures

e.g. Johnson Productions

Email address

Country

production@northside.ca

Canada

Next: Logo & avatar →

The signup wizard itself. Six short steps; the time estimates next to each step are the product's own, and they add up to about five minutes. That is the workspace setup for a new company: this wizard, pre-filled by your group profile. Operational adoption follows at the team's own pace.

Motion Media Group

Tubes Portfolio · portfolio rollup, drill-down into every production

Off

Vendor

Portfolio

TUBES PRODUCTION

Company A

3 productions connected

TUBES PRODUCTION

Company B

1 production connected

TUBES PRODUCTION

Company C

2 productions connected

NEXT SIGNING

Joins via your signup link

Workspace setup in minutes

CHAPTER 4 · BUDGETS & MOVIE MAGIC

Build the budget, or import it

A team can build its budget in Tubes: budget lines organised by cost group, versions to compare scenarios, a locked version as the approved baseline, and a work budget for the team's day-to-day view. Or, and this is the path we expect most of your teams to take, it **uploads its existing Movie Magic budget**, which becomes the live baseline in minutes. Nobody rebuilds anything.

Movie Magic is still widely used for building budgets, and teams that like it can keep it. The difference is everything that happens after the budget. Keep the tools that work; connect the information that matters.

Projects in Production

Demo Tubes



Create a budget

Start from a template, copy an existing one, let AI draft it, or import Movie Magic.

Generate AI Budget

+ Create New Budget

All (8)

Development (3)

Production (4)

Post Production (1)



Fox and the Forest

Development

Project start

22 feb 2026

Delivery

20 jun 2026



The Secret of the Wadden, Part 1

Production

Project start

10 sep 2024

Delivery

13 feb 2025



Echoes of Tomorrow

Post Production

Project start

3 jan 2025

Delivery

19 sep 2025

The projects home of a production company: every production with its status and dates. A budget starts from a template, a copy of an earlier production, an AI draft, or a Movie Magic import. Demo data, illustrative.

 Budget

© Additional costs

€ 64.625

Budget incl. additional

€ 76.600

Sales incl. additional

Lock version

Budget published, editing not possible

Sort: Cost group

Hide Sales

ITEM	QTY	UNIT	UNIT PRICE	BUDGET	SALES
DEVELOPMENT				€ 35.700	€ 44.800
Head writer Treatment + pilot	20	Days	€ 850	€ 17.000	€ 22.000
Script coach 2 sessions per episode	12	Sessions	€ 600	€ 7.200	€ 9.000
Format bible Design + rights	1	Fixed	€ 11.500	€ 11.500	€ 13.800
RECORDING ON LOCATION				€ 18.550	€ 26.050
Camera set 01 2x FX9 + lenses	7	Days	€ 1.850	€ 12.950	€ 18.200
Sound + DIT Location sound	7	Days	€ 800	€ 5.600	€ 7.850
STORY & RIGHTS				€ 1.000	€ 1.250
MONTAGE				€ 3.500	€ 4.500
Totals				€ 58.750	€ 76.600

The budget builder: cost groups with budget and sales side by side, and a locked, published version as the approved baseline. Whether a budget is built here or arrives through Movie Magic import, this is the live baseline that commitments, invoices and the forecast attach to. Demo data, illustrative.

Movie Magic

A budgeting document. Still widely used for building one.

Built for exactly that: constructing and pricing a budget.

The line producer's own working tool.

Its scope ends at the budget; the financial process continues elsewhere.

Tubes

A live system. Imports that budget and connects it to POs, invoices, forecasts and final cost.

Multi-user, cloud, one workspace per company.

Shared by production, finance, and, rolled up, the group.


Adds planning, call sheets and the crew app on the same data.

MMG follows every production live in Tubes Portfolio, nobody has to send a file.

CHAPTER 5 · COST CONTROL IN REAL TIME


Six numbers, from first budget to final cost

How it works: every purchase order and every invoice is entered **against a budget line**, that single discipline is what makes everything else automatic. The moment a PO is raised, the committed total and the estimated final cost move. The team sees its own variance live; nobody waits for a cost report to find out where they stand.

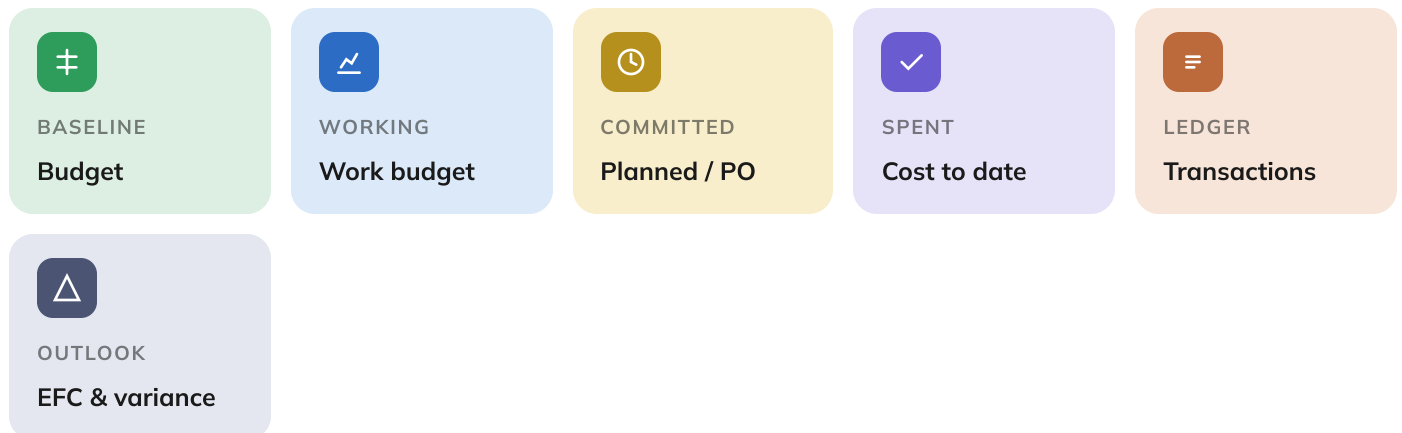

The model is always the same: **approved budget → work budget → committed (PO) → actuals (CTD) + ETC → EFC**, with variance and the cash requirement

following from it. Transactions are not a stage after CTD; they are the input that becomes CTD. The forecast stays anchored to actual costs and commitments, while ETC captures what the team still expects to spend.

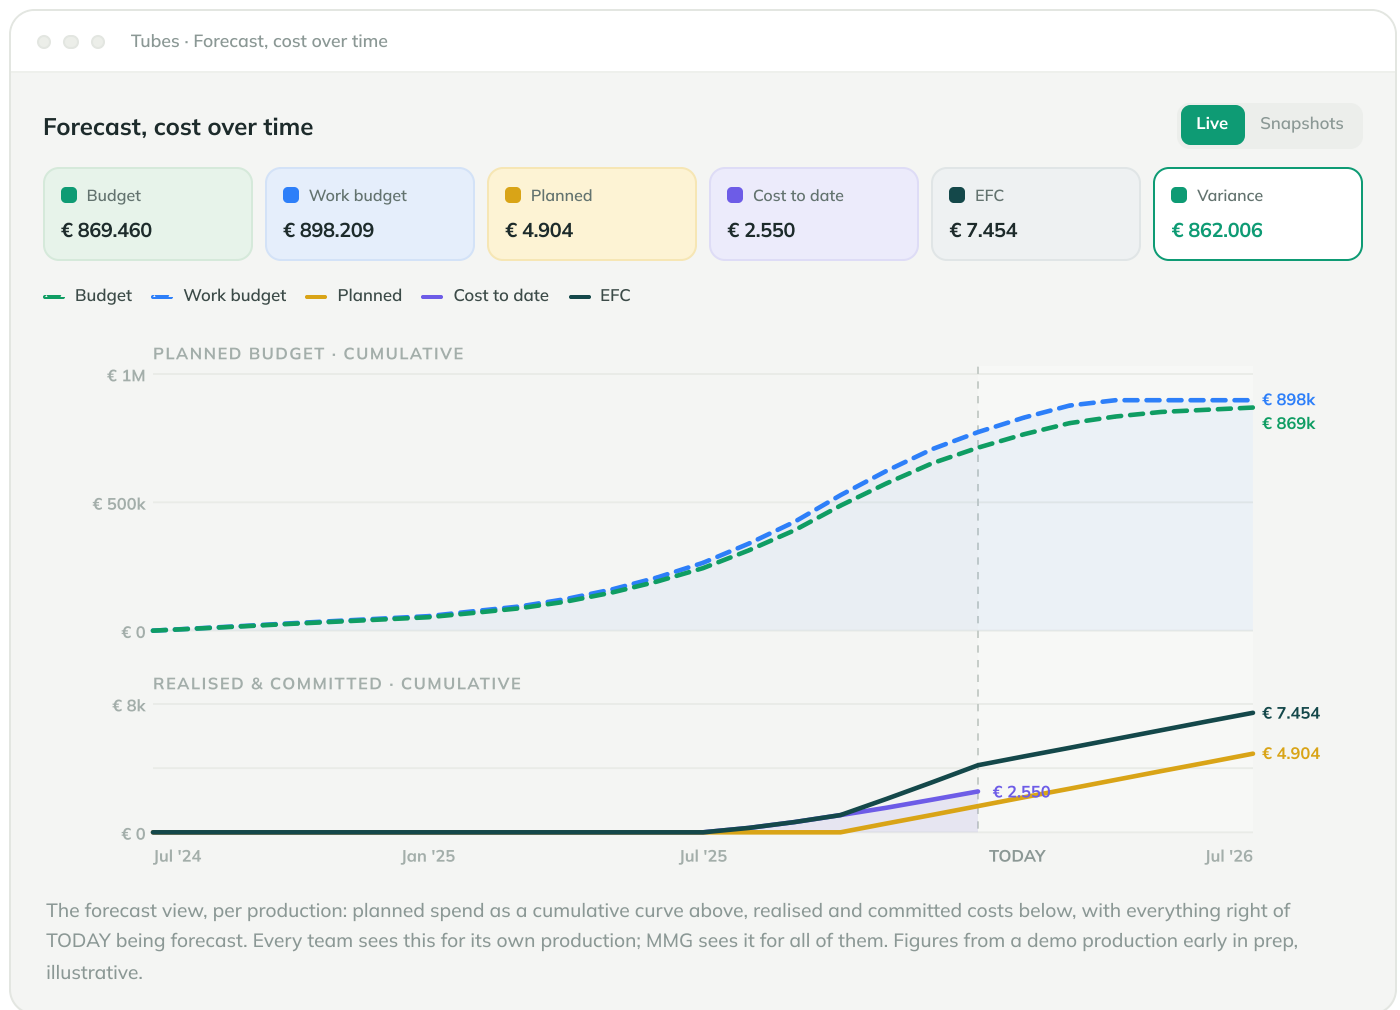


CHAPTER 6 · INVOICES & ACCOUNTING

From inbox to books, without re-keying

How it works: an invoice is dropped in (or mailed in), and Tubes reads it, supplier, amounts, dates, and proposes the budget line it belongs to. A person confirms; approval rules route it to whoever has to sign off at that amount. Once approved, it counts in cost to date and the forecast, immediately.

If the company uses **Xero or other accounting software**, the connection keeps the production ledger and the books aligned, no double entry, no month-end surprise where the two disagree. Teams that prefer exports get exports.

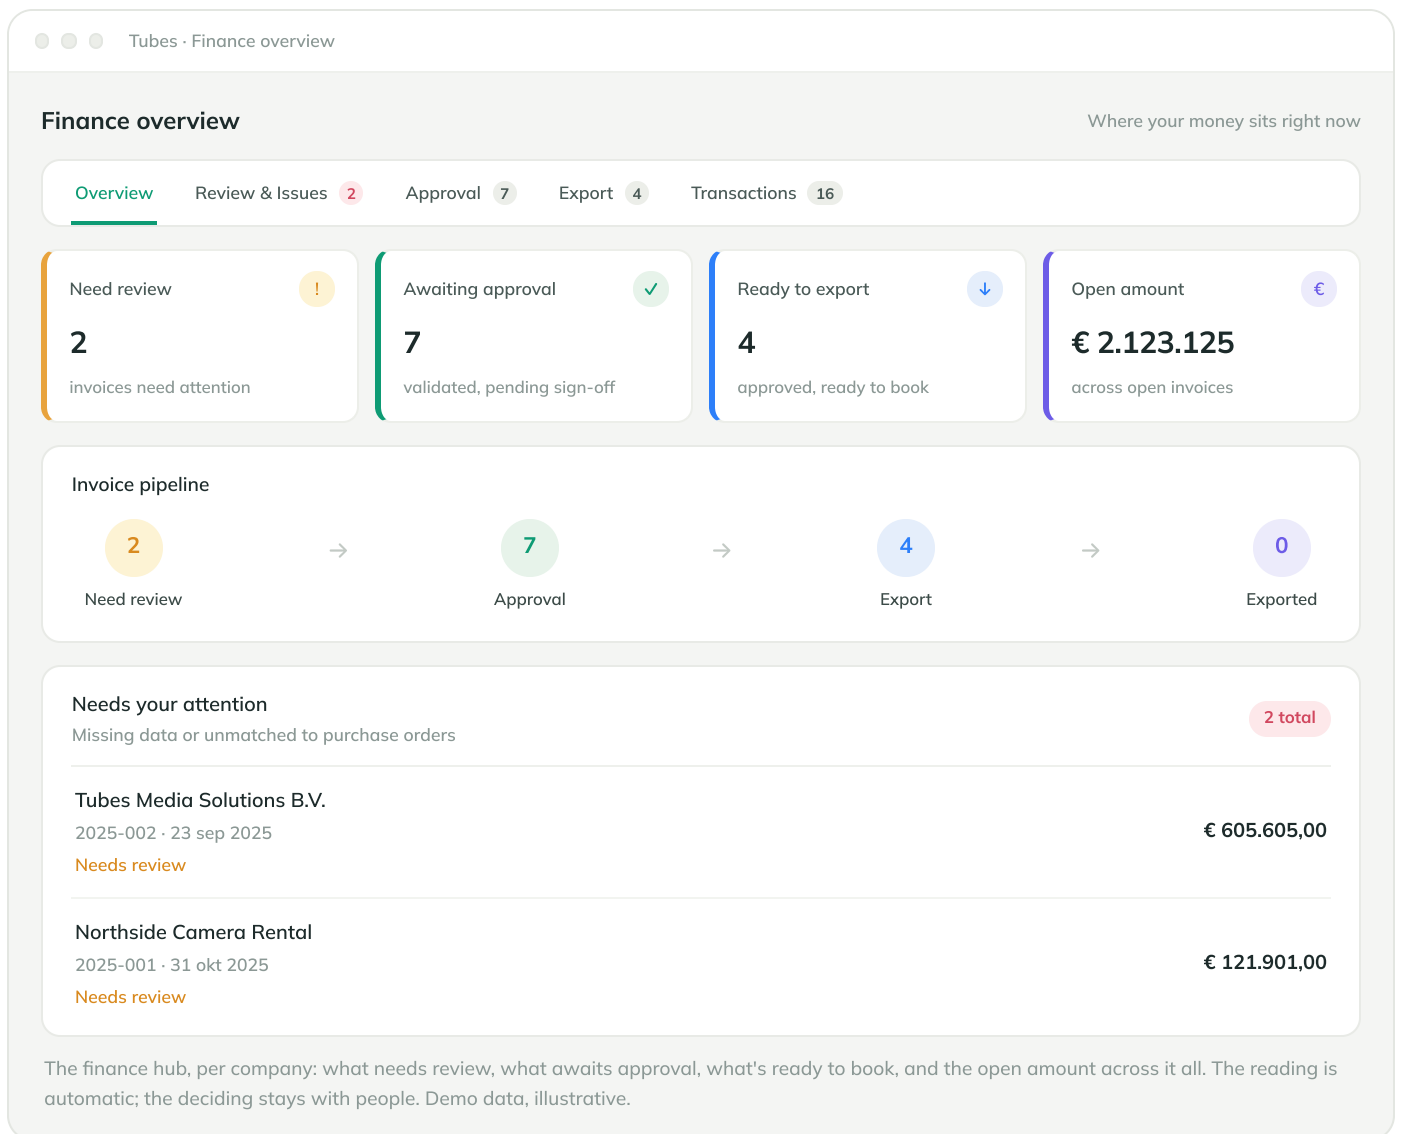

CHAPTER 7 · THE PORTFOLIO DASHBOARD

One dashboard over every connected production

From the portfolio workspace, every production of every connected company is followed **in real time**, one dashboard for progress across the slate. It's not a report that someone assembles: the portfolio view is built from the same live data the production teams work in every day.

PRODUCTION	STATUS	BUDGET	COMMITTED	COST TO DATE	EFC	VARIANCE
Northern Crossing Company A · Feature	● Production	\$8,400,000	\$6,120,000	\$4,385,200	\$8,361,000	+\$39,000
The Long Season Company A · Series, 8 eps	● Production	\$12,000,000	\$9,870,000	\$7,214,900	\$11,986,000	+\$14,000
Salt Water Company B · Feature	● Post production	\$5,150,000	\$5,020,000	\$4,890,400	\$5,102,000	+\$48,000
Fireline Company C · Documentary	● Approved	\$1,900,000	\$310,000	\$122,600	\$1,900,000	—
Portfolio		\$27,450,000	\$21,320,000	\$16,613,100	\$27,349,000	+\$101,000

Illustrative figures. In the live product every number drills down, portfolio → company → production → budget line → the individual invoice or PO behind it.

Tubes · Cost type detail, the bottom of the drill

Project: Fox and the Forest · Forecast · Cost type: 1002, BUDGET DEVELOPMENT

BUDGET

WORK BUDGET

PLANNED

COST TO DATE

EFC

VARIANCE

€ 10.000

€ 10.240

€ 3.000

€ 2.400

€ 5.400

€ 4.600

Cost to date

Planned

Remaining budget

1 planned cost not yet linked to a transaction

Link now

Planned costs & PO's

2 items · 1 to link

To link

Scenario workshop, writers room

Storyline BV · 3 days, incl. location

€ 2.000

Linked

Research trip Ardennes

Recce + location photos · € 900 linked

€ 1.000

Expectations total

€ 3.000

Cost to date

Transactions linked to planned costs

Invoice, writers room day 1-2

Storyline BV · Invoice 2026-114 · linked to: Scenario workshop

€ 1.500

Freelance script editor

M. van Dijk · Invoice 2026-131 · linked to: Research trip Ardennes

€ 900

Cost to date total

€ 2.400

The bottom of the drill: one cost type of one production. Every PO and every invoice is linked to the budget line it belongs to, which is exactly why the portfolio numbers above can be trusted. Anything unlinked is flagged until someone deals with it. Demo data, illustrative.



Early warnings

The dashboard flags a production the moment its forecast moves past budget, at commitment time, weeks before it would surface in a cost report.



AI analysis

AI analyses support the group view: the assistant reads along with the numbers and flags what deserves attention, at group level and on set.

The same slate also reads as a **cashflow and margin forecast overview per production company**, switchable between month, quarter and year. For a capital-recycling model, this is the view that matters: when does cash go out, when does it come back, and what margin is each company on course to deliver.

Month

Quarter

Year

COMPANY	SEP 2026	Q4 2026	FY 2026	MARGIN · FY 2026
Company A 2 productions in production	-\$1,240,000	-\$2,850,000	-\$5,400,000	14.2%
Company B Delivering	+\$380,000	+\$1,050,000	+\$1,620,000	11.8%
Company C Pre-production	-\$210,000	-\$640,000	-\$980,000	17.5%
Portfolio	-\$1,070,000	-\$2,440,000	-\$4,760,000	14.6%

Illustrative figures. Company A is in peak production (cash going out); Company B is delivering (cash coming back). The margin column is the forecast at completion, per company, from the same live production data.

The same forecasts add up to the picture an investor actually asks about: how much capital is at work across the slate, and when it comes back.

Capital at work across the slate

Deployed capital per month, deliveries bringing it back. Illustrative



Built from the production forecast, expected payment timing and funding tranches; receivables and incentives can be added where available. Deliveries bring capital plus margin back, and the live forecast shows when it comes free and when new commitments will need it. Illustrative.

And because every production carries its running time and episode count, the dashboard also shows the **unit economics**, the numbers your acquisitions side thinks in:

SERIES

\$1.56M / episode

The Long Season, forecast cost per episode, against a \$1.50M budget target.

FEATURE

\$79k / finished minute

Northern Crossing, 106 finished minutes on an \$8.4M budget.

COMPARABLE

Same metric, every production

Price per minute and per episode, computed from live forecasts, comparable across the whole slate.

Budgets and status snapshots can also be shared with outside stakeholders through **read-only links**, so investor reporting draws on live numbers instead of assembled spreadsheets.

CHAPTER 8 · AI IN TUBES

AI that does the reading, not the deciding

AI in Tubes is practical. It takes over the reading and drafting work that eats production-finance hours, and it leaves every decision with a person. In the

product, violet marks the assistant, so it is always clear when a suggestion came from AI.



Draft budgets

Describe the production, the format and the target amount, and the assistant drafts a first budget the team refines. Faster to a workable starting point, especially for recurring formats. This is the newest assistant in Tubes: it delivers a draft, never a decision.



Read invoices and documents

Invoices are read automatically: supplier, amounts, dates and a proposed budget line. A person confirms, and approvals stay human.



Watches along during cost control

While a production runs, the assistant reads along with the numbers against the budget and flags what deserves attention: per team on set, and rolled up at group level for MMG.



Analysis at wrap

When a production wraps, the assistant compares budget to final cost per cost type and distils what the next production should do differently.



Automatic translation

Working languages stop being a barrier: the assistant translates between the ten supported languages, so a Dutch production team and a Canadian head office read the same information.

Every suggestion stays visible, attributable and reversible, with usage on monthly AI credits per workspace, so the cost side stays predictable.

Our vision behind all of this is in our tagline: **empowering productions**. Production teams should spend their time making things, not reconciling spreadsheets, and the people financing them should never have to wait a month to know where they stand. AI is how we push that further. Where it is heading, when it is relevant to how a team works: operating Tubes from a chat. Ask a question, get the live answer; give an instruction, and the assistant prepares it for a person to approve.

How is The Long Season doing against budget?

It's **\$14k under**, the tightest margin on the slate. EFC is **\$11.99M** against a **\$12.0M** budget, with cost type 2000 CREW closest to its line. Want the breakdown per line?

Yes, and prepare a note for Thursday's production meeting.

Breakdown is open on your screen. The note is drafted and waiting for your approval before it goes to the team.

CHAPTER 9 · PLANNING, CALL SHEETS & CREW

Operations on the same data as the money

How it works: the production plans its days in Tubes, builds call sheets from that planning, and publishes them when ready. Published call sheets and schedules land directly on the crew's phones through the Tubes mobile app, no PDF chains, no "which version is current".

Because planning lives next to the budget, the operational picture and the financial picture stop being two different documents maintained by two different people.

Tubes · Planning

Planning10 aug 2026 – 16 aug 2026

CalendarCallsheets

MONDAY 10	TUESDAY 11	WEDNESDAY 12	THURSDAY 13
07:00 – 19:00 Shoot day 12 · The Long Season Studio 4	07:00 – 19:00 Shoot day 13 · The Long Season Studio 4	09:00 – 13:00 Location scout Unit manager	08:00 – 18:00 Shoot day 14 · The Long Season Location: Westergas
20:00 Dailies review Online · director & DoP		14:00 – 17:00 Tech recce The Secret of the Wadden	10:00 Cast fitting Reality & Competitie

Callsheets

Per shooting day, status, distribution and crew

+ New callsheet

10 AUG	Callsheet #12 The Long Season · S1	07:00 / 19:00	Sent
13 AUG	Callsheet #14 The Long Season · S1	08:00 / 18:00	Draft
17 AUG	Callsheet #01 The Secret of the Wadden · S1	06:30 / 17:30	Planned

One week of a production: shoot days, prep and post side by side, and the callsheets that go with them. "Sent" means the crew already has it on their phones. Demo data, illustrative.

CHAPTER 10 · CURRENCIES & LANGUAGES

Built for a slate that crosses borders

MMG finances productions across jurisdictions, Canada, Puerto Rico, India, Africa. Tubes is built for that reality rather than adapted to it.

CURRENCY

Local currency + FX

Each production house works in its local currency, with fixed exchange rates per production, so budgets do not drift with the currency market.

LANGUAGE

10 languages


The major Western languages, set per workspace or per individual user, a Dutch line producer and a Canadian accountant can work in the same production, each in their own language. Other languages are optional additions.

GETTING STARTED

Built for a fast start

A workspace is live in minutes, not weeks. No complex implementation project.

How the currency side works: a production company budgets, raises POs and books invoices entirely in its **local currency**, the numbers its vendors, crew and accountant actually use. Tubes handles the exchange rates on top of that, fixed per production, so the group rollup reads in one reporting currency without anyone converting anything by hand.

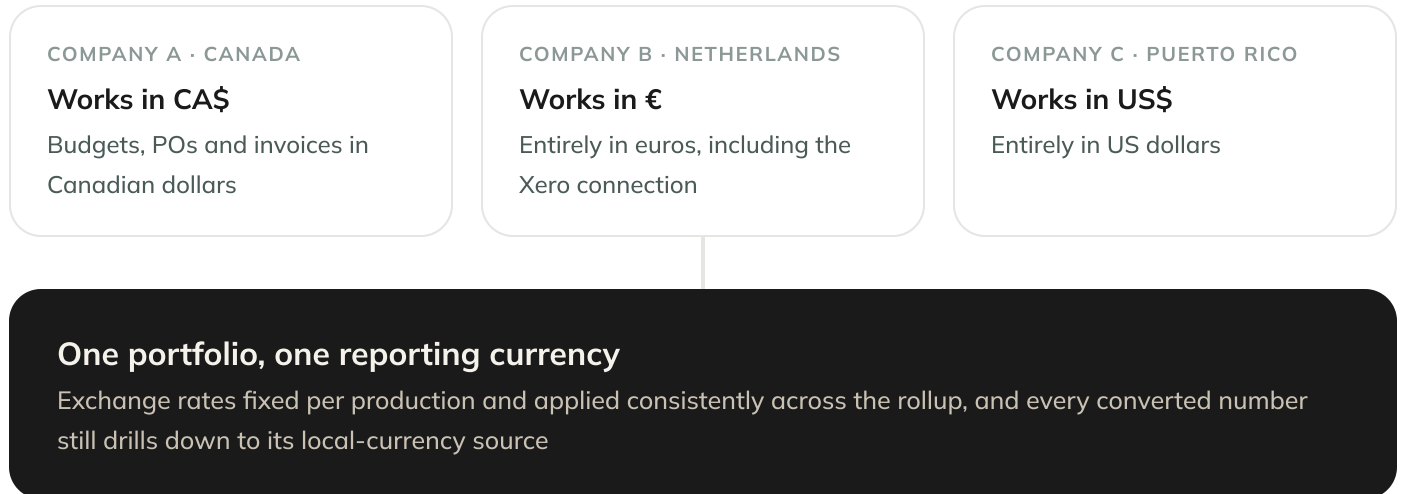


CHAPTER 11 · DATA SEPARATION & PERMISSIONS

Who sees what, by design

Every production company runs in its **own, separated workspace**. Its data is its own; MMG's portfolio workspace sees the rollup and can drill into the productions it finances, it does not operate inside the company's books, and companies do not see each other.

Inside each workspace, **role-based permissions** decide who can see and do what: a line producer sees their production, a department head can be limited to their own work budget, an accountant sees finance but not necessarily rates, and approval rules put a named person between a large commitment and the money. The same discipline that protects a production internally is what makes group-level transparency acceptable to the teams. Read-only means the data: MMG sees and drills into everything it finances, and edits nothing.



MMG · Tubes Portfolio

Sees the rollup and drills into its own slate; never operates inside the companies' books. Companies do not see each other.

ROLE	PRODUCTION DETAIL	RATES & SALARIES	FINANCE	GROUP ROLLUP
Line producer runs the production	● Full	● Full	● Full	—
Department head own work budget	● Own lines only	—	—	—
Accountant books & export	● Full	—	● Full	—
MMG · Tubes Portfolio read-only oversight	● Read-only drill-down	—	—	● Full

How to read this: "Full" means the role sees and works in that area; "Own lines only" limits a department head to their own budget lines; the dash means no access. Illustrative permission set: every workspace defines its own roles and approval rules, this is a typical shape, not a fixed one.

CHAPTER 12 · ADOPTION PATH & PILOT

Gradual by design, starting with a pilot

Nobody changes their whole way of working in week one. This is how teams actually take it up; past phase one, each team sets its own pace.

1

Import and see

Workspaces created via your signup link. Current Movie Magic budgets imported. Costs start landing against budget lines. Your portfolio view is live.

First

2

Control

Approval rules, forecasts and expectations, the accounting connection. Overruns surface at commitment time, group-wide.

Then

3

Run

Day planning, call sheets and the crew app, production operations on the same data as the money.

When a team wants it

The pilot

The quickest way to judge this is to look at one of your own productions through it.

- ✓ **Pick one production you finance.** Its team signs up through your link and imports its current budget.
- ✓ **Set up the MMG portfolio workspace,** configured with your standard setup and templates, ready to roll out further later.
- ✓ **Follow the production live:** budget, commitments, cost to date and forecast, from the portfolio dashboard down to the invoice.
- ✓ **Then decide.** If the picture isn't sharper than what you have today, that is the end of it.

Plan the walkthrough

or write me directly, joachim@tubes.media

What's in the box

Straight from the product's own navigation. Unlabelled items are available in Tubes today; younger functionality is marked as early version or in development. Teams use what fits and ignore the rest; nothing has to be switched on all at once.

Develop & budget

- ✓ Project setup, briefing and funding
- ✓ Format templates, reusable across productions
- ✓ Budget builder with versions and a locked baseline
- ✓ Movie Magic budget import
- ✓ Budget compare for scenarios
- ✓ Commercial proposals for clients and commissioners
- ✓ AI budget drafting support (early version)
- ✓ Project documents, images and links in one place

Plan & produce

- ✓ Day planning and scheduler
- ✓ Scenes & breakdown, stripbook (in development)
- ✓ Casting, recruitment and cast & crew management
- ✓ Locations
- ✓ Call sheets with status and distribution
- ✓ Crew app: schedules and callsheets on every phone
- ✓ Editing and delivery tracking
- ✓ Production dashboard per shoot day

Control the money

- ✓ Work budgets per team member or department
- ✓ Planned costs and purchase orders
- ✓ Operational invoice processing with automatic reading
- ✓ Approval rules and transaction approval
- ✓ Transactions linked to budget lines
- ✓ Live forecast and EFC, with views per role
- ✓ Cost reports: budget versus actuals per period, with historical snapshots
- ✓ Local currency per company, fixed exchange rates per production
- ✓ Xero and other API accounting connections

Oversee & share

- ✓ MMG Tubes Portfolio: rollup over every company and production
- ✓ Cashflow and margin forecasts by month, quarter and year
- ✓ Early warnings when a forecast moves past budget
- ✓ AI analyses (early version)
- ✓ Price per minute and per episode across the slate
- ✓ Read-only share links for investors and clients
- ✓ Role-based permissions and separated workspaces
- ✓ Signup links, standard setup and group-wide templates

